

Agile Backlog Creation & Sprint Simulation in Jira

Digital Art Commission & Watermarking Portal — Problem Statement #58

Student	Shrikar Desai
SRN	PES1UG24CS916
Jira Scrum Space	SCRUM25
Sprints completed	2
Total story points	37

This report documents the Jira Scrum backlog, epics, user stories, story-point estimation, two simulated sprints, sprint progression, burndown analysis, velocity, and reflection.

1. Lab Objective and Scenario

The Lab 2 handout instructs students to convert Lab 1 functional requirements into Agile Epics and User Stories, prioritize and estimate them, simulate a sprint, monitor progress with a Burndown Chart, and reflect on the outcome. Required evidence includes the Jira backlog, story-point assignments, Active Sprint view, Burndown Chart, and a brief reflection.

The scenario from Lab 1 is the Digital Art Commission & Watermarking Portal. The Lab 1 requirements cover WIP watermarking, creative-brief submission, WIP uploads, milestone payments, final-asset unlocking, expiring signed S3 URLs, and protection against unauthenticated access.

Requirement	Priority	Theme represented in Jira
FR-001 - Dynamic diagonal WIP watermark	High	WIP Draft & Watermarking
FR-002 - Client submits visual creative brief	High	Commission Intake
FR-003 - Artist uploads WIP drafts	High	WIP Draft & Watermarking
FR-004 - Milestone payment and status	High	Milestone Payment & Asset Release
FR-005 - Unlock final asset after payment	High	Milestone Payment & Asset Release
NFR-001 - Expiring signed S3 URL (60 min)	High	Milestone Payment & Asset Release
NFR-002 - Prevent unauthenticated access	High	Platform Reliability & Security

Lab 1 identifies Client Buyer, Digital Artist, Payment Gateway, and Object Storage (S3) as actors. It also defines six primary use cases and the required include/extend relationships.

2. Jira Epics and User Stories

Five Epics were created in the SCRUM25 space, with seven User Stories linked beneath the appropriate themes.

Epic	Purpose
Commission Intake	Client creative-brief submission and intake
WIP Draft & Watermarking	WIP draft upload and dynamic watermarking
Milestone Payment & Asset Release	Payment processing, final release and secure download
Revision Management	Revision-request handling
Platform Reliability & Security	Availability, failover and platform protection

User Story	Points	Priority
Submit Creative Brief	5	High
Apply Dynamic Watermark	3	Medium
Upload WIP Progress Draft	5	Medium
Process Milestone Payment	8	Medium
Generate Expiring Download Link	5	Medium
Submit Revision Request	3	Medium
Maintain Platform Availability	8	Medium
Total	37	—

The seven stories use Fibonacci-style estimates: 3, 5, and 8 points. The overall planned workload is 37 story points.

3. Jira Backlog Evidence


The List view below shows the full SCRUM25 backlog: all five Epics with their linked User Stories, priorities, and status. This confirms the 5 Epics + 7 User Stories structure described above, prior to the sprint simulation.

Ask AI, Search work, Filter, Group										
	Work	Assignee	Reporter	Priority	Status	Resolution	Created	Updated	Due date	
▼	SCRUM25-1 Commission Intake	Unassigned	Shikhar Desai	Medium	To Do	Unresolved	Aug 30, 2026, 12:48 PM	Aug 30, 2026, 12:48 PM	None	...
	SCRUM25-2 Submit Creative Brief	Unassigned	Shikhar Desai	High	Done	Done	Aug 30, 2026, 12:52 PM	Aug 30, 2026, 1:08 PM	None	...
▼	SCRUM25-3 WIP Draft & Watermarking	Unassigned	Shikhar Desai	Medium	To Do	Unresolved	Aug 30, 2026, 12:48 PM	Aug 30, 2026, 12:49 PM	None	...
	SCRUM25-4 Apply Dynamic Watermark	Unassigned	Shikhar Desai	High	Done	Done	Aug 30, 2026, 12:52 PM	Aug 30, 2026, 1:09 PM	None	...
	SCRUM25-5 Upload WIP Progress Draft	Unassigned	Shikhar Desai	High	Done	Done	Aug 30, 2026, 12:53 PM	Aug 30, 2026, 1:10 PM	None	...
▼	SCRUM25-6 Milestone Payment & Asset Release	Unassigned	Shikhar Desai	Medium	To Do	Unresolved	Aug 30, 2026, 12:48 PM	Aug 30, 2026, 12:49 PM	None	...
	SCRUM25-7 Process Milestone Payment	Unassigned	Shikhar Desai	High	Done	Done	Aug 30, 2026, 12:54 PM	Aug 30, 2026, 1:10 PM	None	...
	SCRUM25-8 Generate Expiring Download Link	Unassigned	Shikhar Desai	High	Done	Done	Aug 30, 2026, 12:54 PM	Aug 30, 2026, 1:14 PM	None	...
▼	SCRUM25-9 Revision Management	Unassigned	Shikhar Desai	Medium	To Do	Unresolved	Aug 30, 2026, 12:50 PM	Aug 30, 2026, 12:50 PM	None	...
	SCRUM25-10 Submit Revision Request	Unassigned	Shikhar Desai	Medium	Done	Done	Aug 30, 2026, 12:55 PM	Aug 30, 2026, 1:14 PM	None	...
▼	SCRUM25-11 Platform Reliability & Security	Unassigned	Shikhar Desai	Medium	To Do	Unresolved	Aug 30, 2026, 12:50 PM	Aug 30, 2026, 12:50 PM	None	...
	SCRUM25-12 Maintain Platform Availability	Unassigned	Shikhar Desai	Medium	Done	Done	Aug 30, 2026, 12:55 PM	Aug 30, 2026, 1:14 PM	None	...
+ Create		8 of 8								


Jira backlog list: 5 Epics (Commission Intake, WIP Draft & Watermarking, Milestone Payment & Asset Release, Revision Management, Platform Reliability & Security) with their 7 linked User Stories, priorities and status.

4. Sprint 1 - Execution Evidence


Planned: 4 stories / 21 points (Submit Creative Brief - 5, Apply Dynamic Watermark - 3, Upload WIP Progress Draft - 5, Process Milestone Payment - 8). The sprint was simulated by moving work through To Do → In Progress → Done.

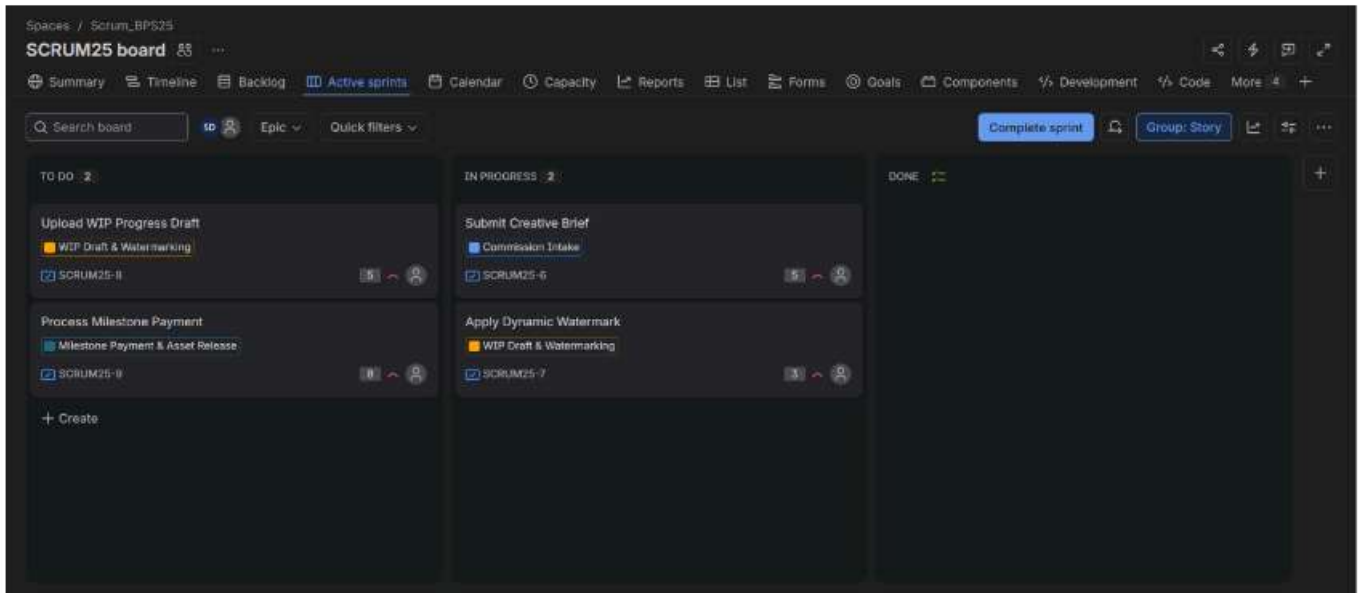


Sprint 1 start: 2 stories in To Do (Upload WIP Progress Draft, Process Milestone Payment) and 2 stories In Progress (Submit Creative Brief, Apply Dynamic Watermark).

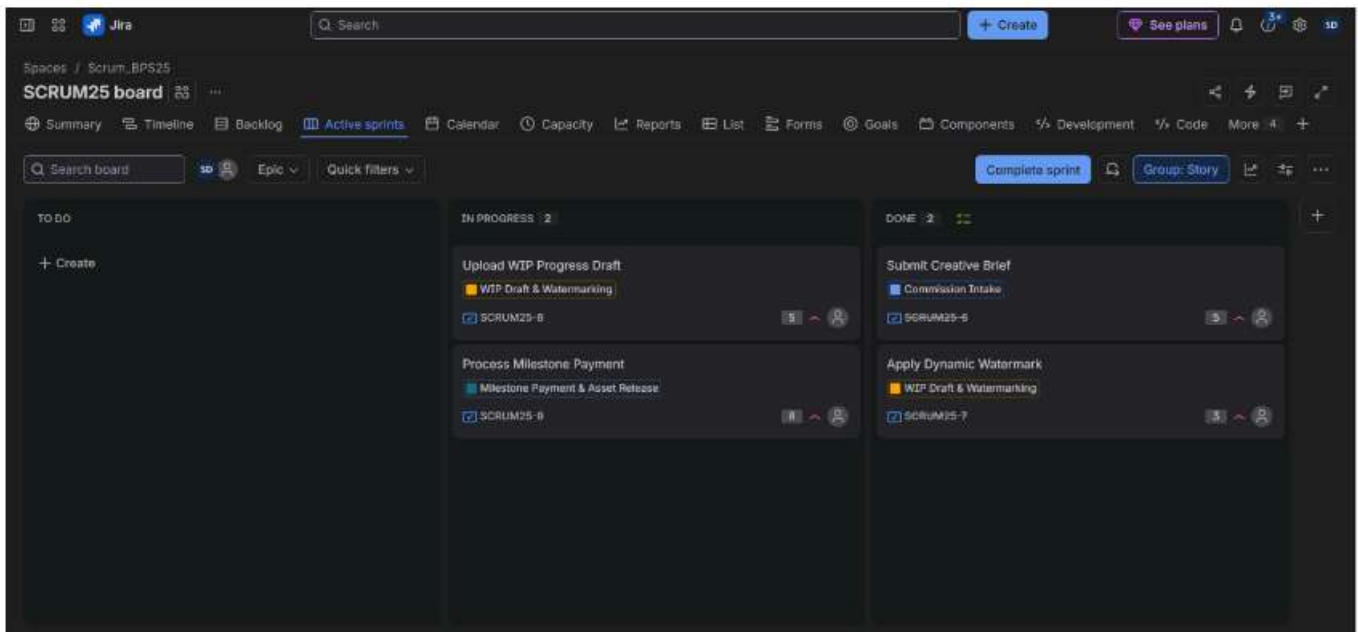

Mid-sprint: 2 stories completed (Submit Creative Brief, Apply Dynamic Watermark) and 2 stories still In Progress.

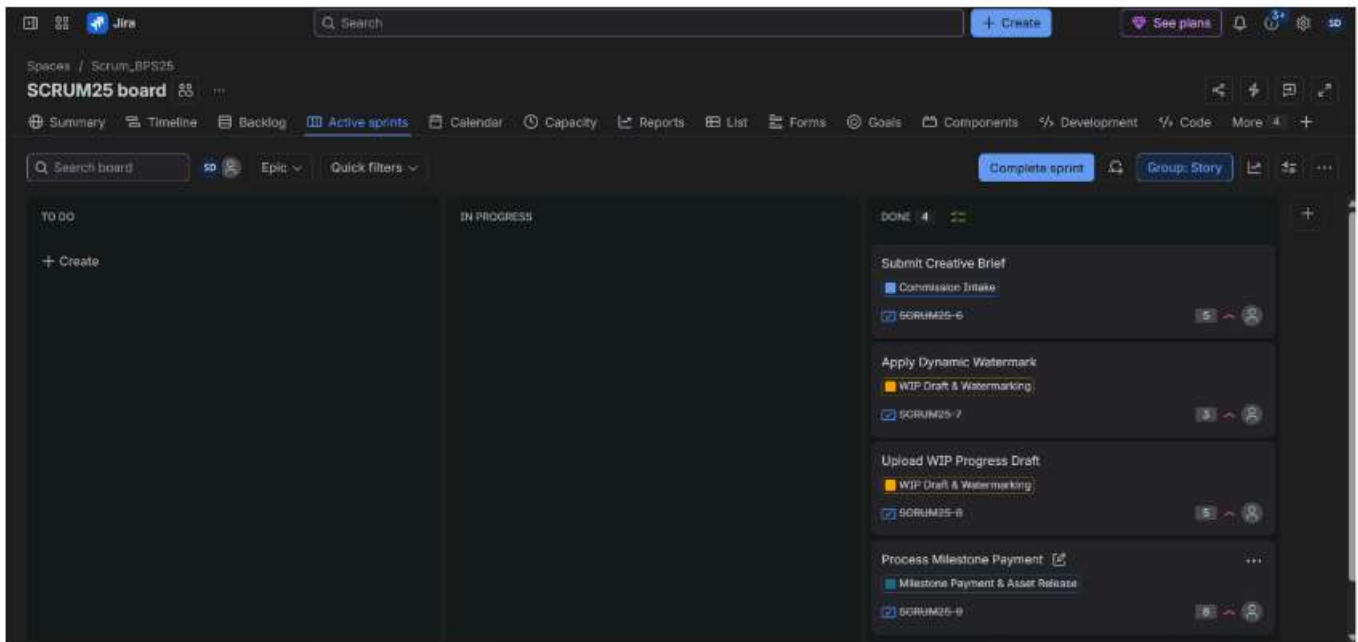

Sprint 1 complete: all 4 planned stories moved to Done.

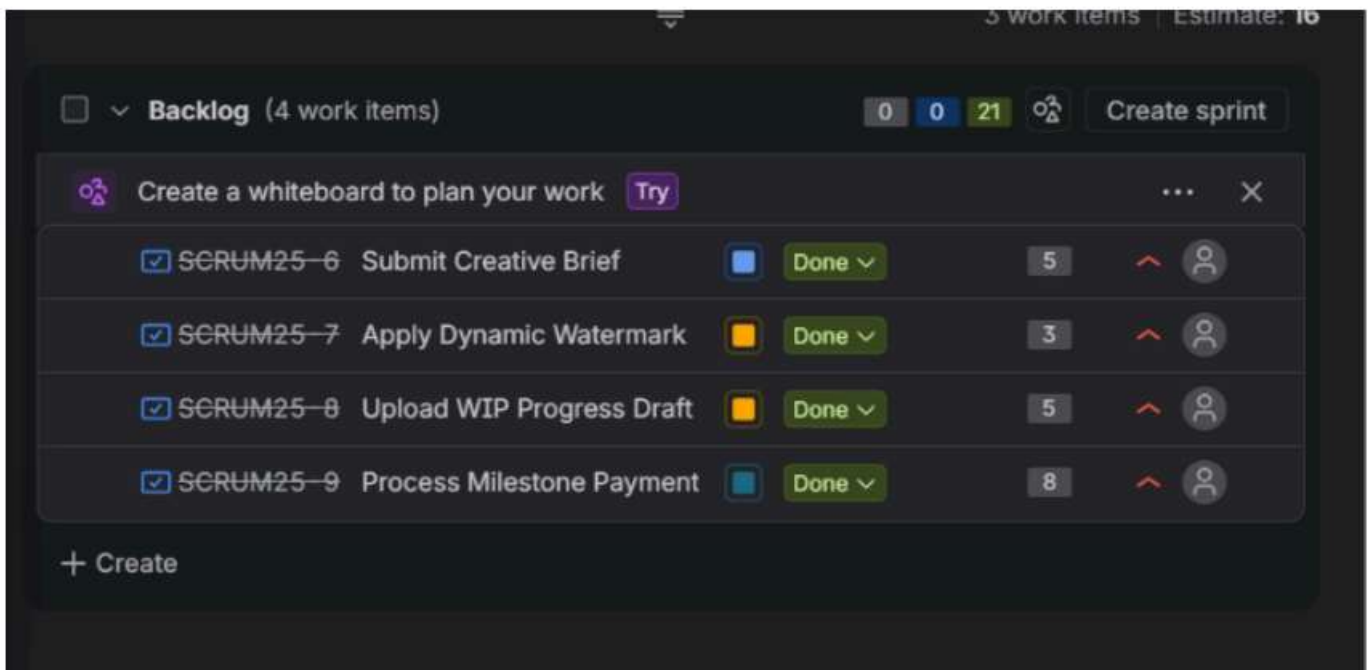


Backlog view confirming all 4 Sprint 1 stories marked Done, 21 story points delivered.


Sprint 1 result: 4/4 stories completed and 21/21 story points delivered.

5. Sprint 2 - Execution Evidence


Planned: 3 stories / 16 points (Generate Expiring Download Link - 5, Submit Revision Request - 3, Maintain Platform Availability - 8). Sprint 2 continued the same simulated Scrum workflow.

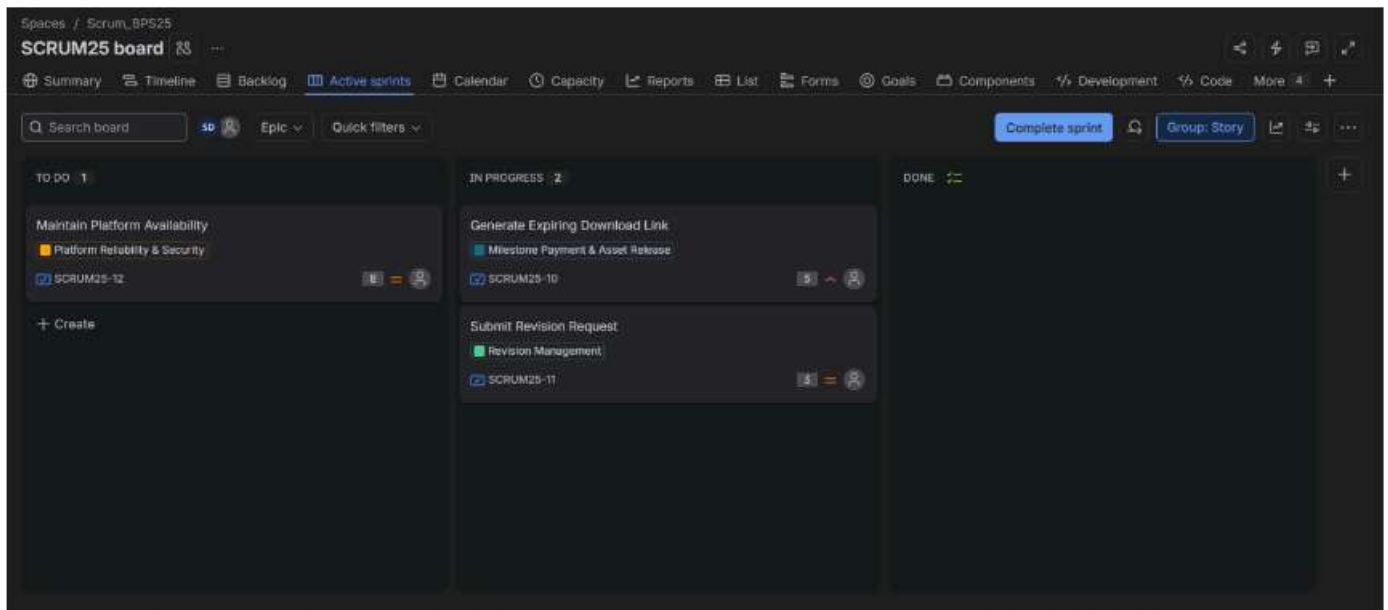


Sprint 2 start: 1 story in To Do (Maintain Platform Availability) and 2 stories In Progress (Generate Expiring Download Link, Submit Revision Request).

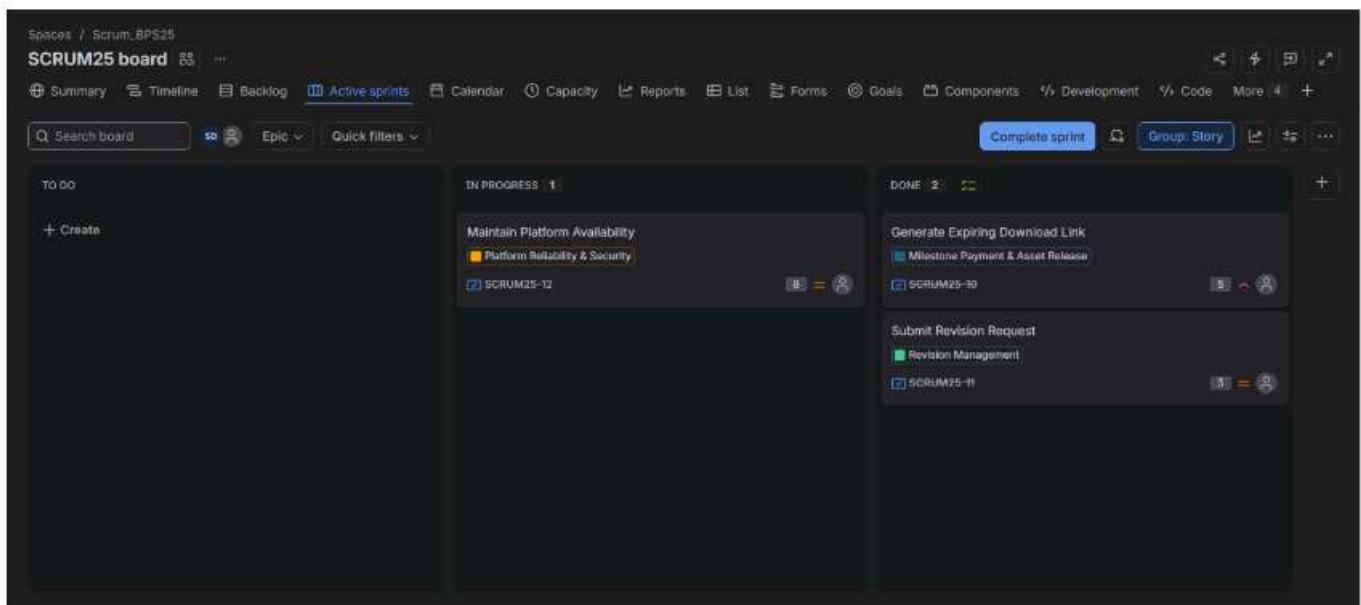

Mid-sprint: 2 stories completed (Generate Expiring Download Link, Submit Revision Request) and 1 story still In Progress (Maintain Platform Availability).

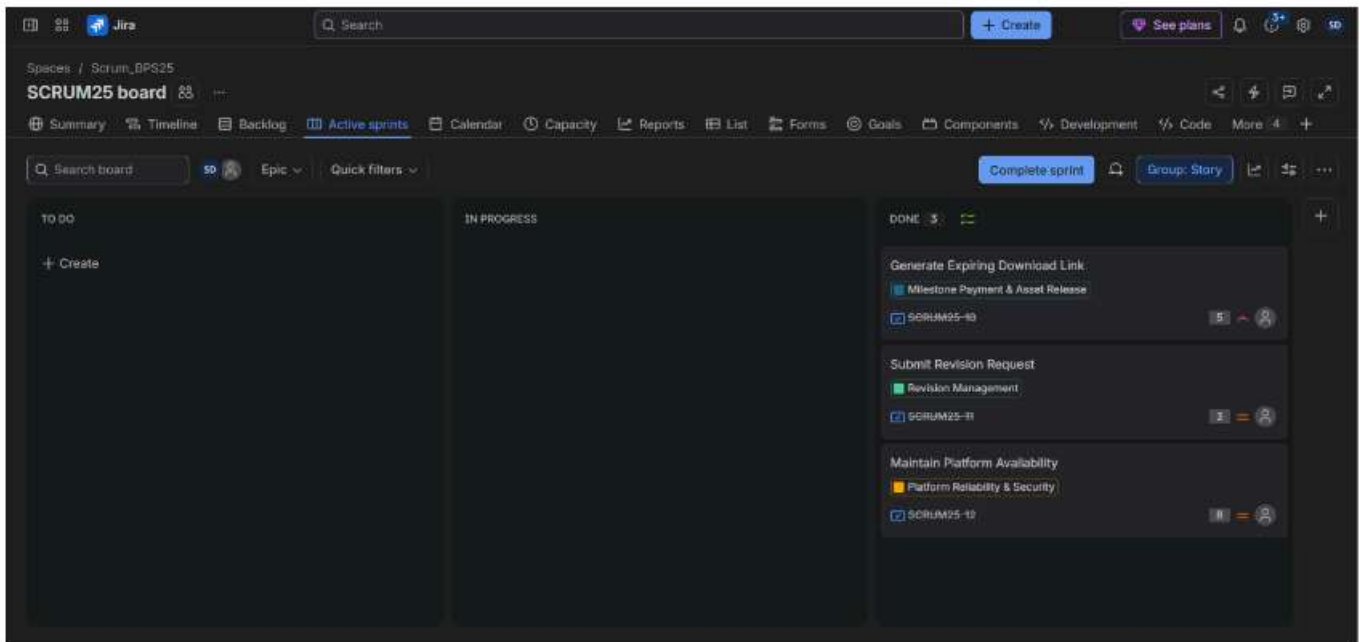

Sprint 2 complete: all 3 planned stories moved to Done.

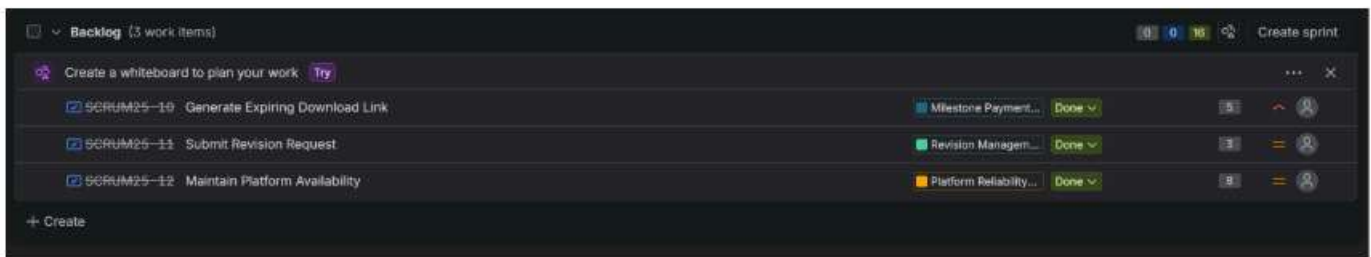


Backlog view confirming all 3 Sprint 2 stories marked Done, 16 story points delivered.

Sprint 2 result: 3/3 stories completed and 16/16 story points delivered.


6. Burndown Chart

The Sprint 2 Burndown Chart tracks total work remaining across the sprint window.

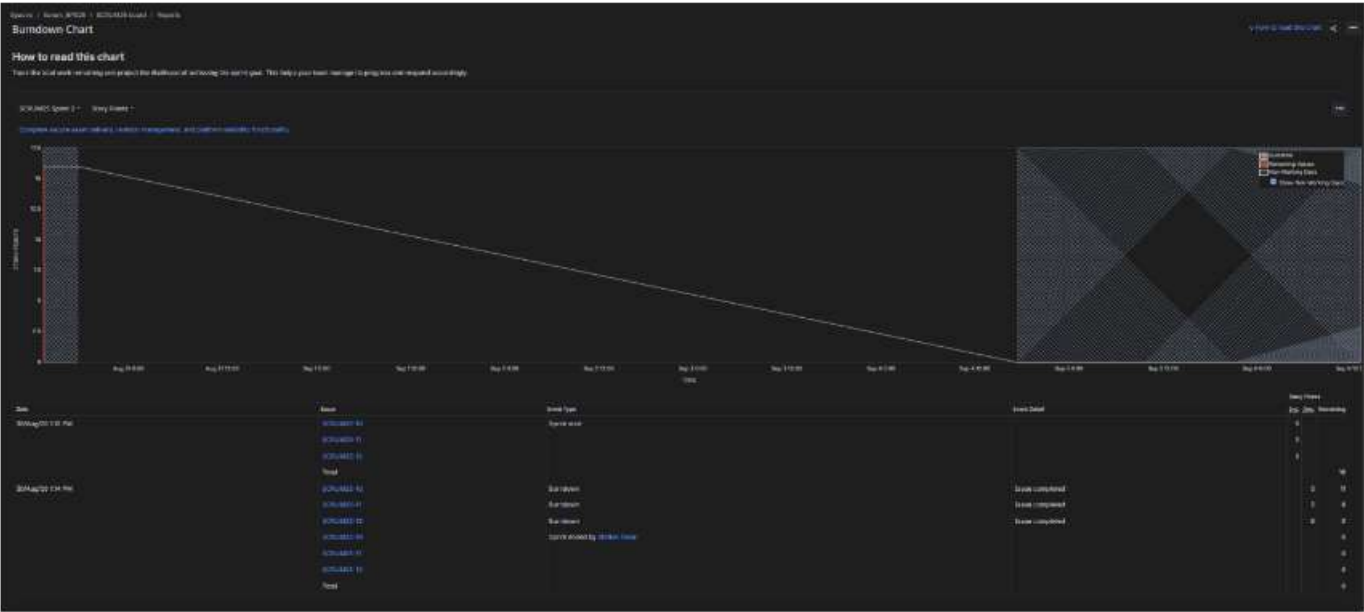


Sprint 2 Burndown Chart: the remaining workload starts at 16 story points and reaches 0 as all three stories are completed.

7. Sprint Report

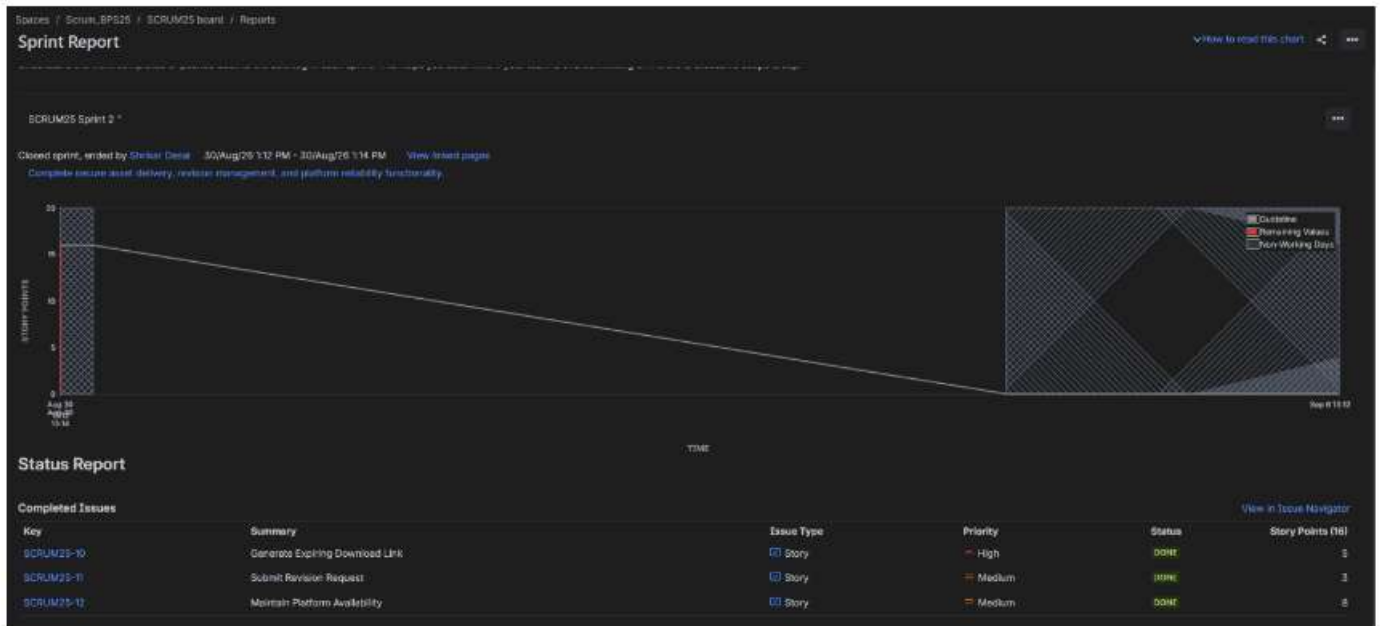


Sprint 2 Sprint Report: Jira records all three stories as DONE and reports 16 completed story points.

8. Velocity Report

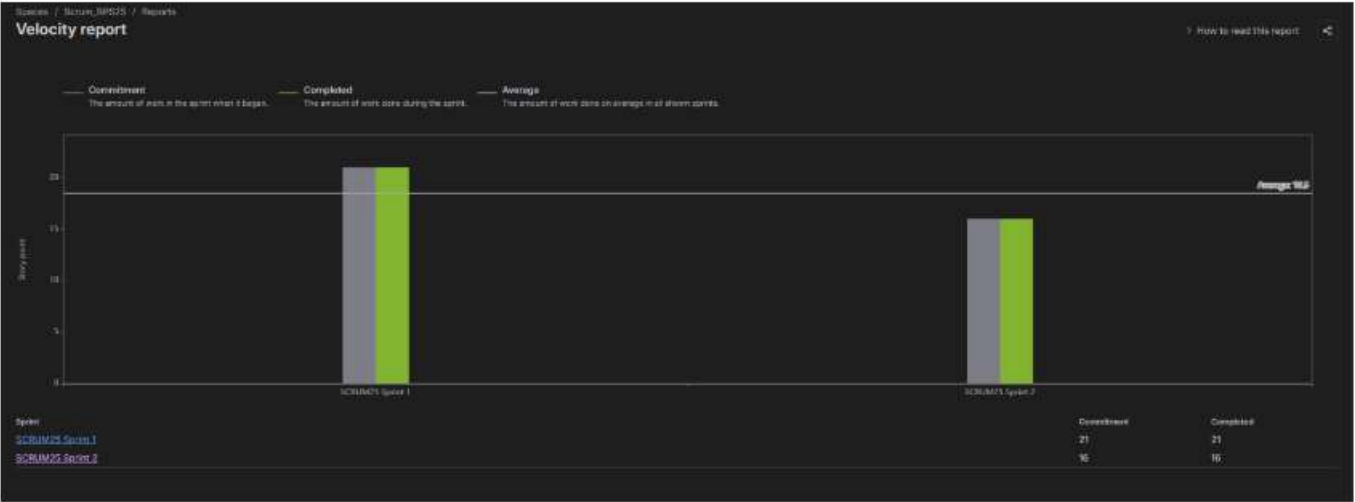

Velocity Report: Sprint 1 committed/completed 21 points; Sprint 2 committed/completed 16 points; average velocity is 18.5 points per sprint.

9. Final Backlog State



After both sprints were completed, the Jira backlog contains no remaining work items.

10. Overall Scrum Results

Metric	Result
Stories created	7
Epics created	5
Total estimated workload	37 points
Sprint 1	21 committed / 21 completed
Sprint 2	16 committed / 16 completed
Overall delivery	37 / 37 points (100%)
Average velocity	18.5 points / sprint

The Jira evidence demonstrates two completed simulated sprints. All committed work was completed, and the final backlog contains no remaining work items.

11. Reflection Questions

1. Did your estimations reflect the actual effort?

Within the simulation, yes. Sprint 1 completed all 21 committed points and Sprint 2 completed all 16 committed points. Thus, the planned estimates matched the simulated workload. Since this lab was a Jira simulation rather than a software implementation, this does not measure real engineering effort.

2. Was your backlog well-prioritized?

Yes. The backlog was organized into five functional Epics and seven User Stories, with higher-impact client-facing items assigned higher priority where applicable. The work was then divided across two sprints.

3. How did your simulated sprint align with your plan?

The execution aligned completely with the plan. Sprint 1 delivered 21/21 points and Sprint 2 delivered 16/16 points. Jira's Sprint Report and Velocity Report confirm these planned-versus-completed values.

4. What insights did the burndown chart give about your team's capacity?

The Sprint 2 burndown reached zero remaining points, showing that the complete 16-point commitment was delivered within the simulated sprint. Across two sprints, the recorded average velocity was 18.5 points per sprint. In a real project, this could provide a baseline for future planning; in this lab it primarily demonstrates the simulation outcome.

Conclusion: the SCRUM25 Jira workspace successfully converted the Lab 1 scenario into an Agile backlog, estimated the work, executed two simulated sprints, and generated the required Scrum progress evidence.

Note : The required BPS number for this submission is 58. I was initially unaware that the BPS number referred to the assigned Problem Statement number, so the PDF filename/project naming may reflect a different number in some places. The work and Jira implementation are based on Problem Statement #58 – Digital Art Commission & Watermarking Portal. I apologize for the oversight and have corrected the PDF filename accordingly.

